



COMSATS University Islamabad, Lahore Campus

Midterm Exam Spring 2024

Course Title:	Software Project Management			Course Code:	CSE494	Credit Hours:	3(2,1)
Course	Ms. Humaira Afzal			Program Name:	BS Software Engineering		
Semester:	7 th	Batch:	SP21-BSE	Section:	A & B	Date:	
Time Allowed:	1.5 hrs.			Maximum Marks:	40		
Student's Name:				Reg. No.			

Instructions / Submission Guidelines:

- Attempt all the questions.
- Use of any communication device is not allowed.
- Manage your time accordingly.
- Return the question paper after exam.

Question. 01

[Marks: 25]

CLO: <6>; Bloom Taxonomy Level: <Applying>

You have been appointed as the Project Manager for a high-priority E-commerce Store development project for a major retail client. The store must be user-friendly, visually appealing, and capable of handling high traffic and secure transactions. It should include features such as a product catalog, shopping cart, payment gateway, customer reviews, and mobile responsiveness. Estimated duration is 6 months according to cost benefit analysis report. After starting the project, you observed that the project can be completed in 4 months using *Schedule Compression*. Develop a strategy for schedule compression. According to the quality report shown in Fig-1:


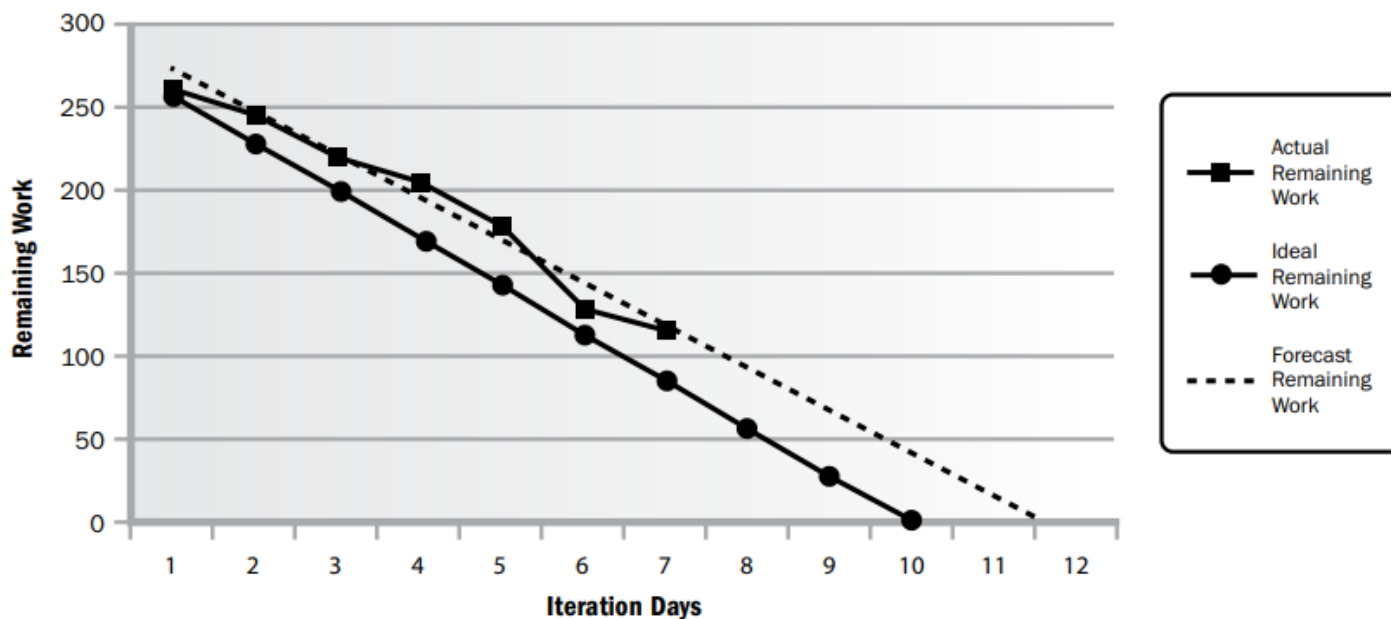


Fig-1

Current project activities are scheduled with relationships [1->2->3->4,5->6->7, 8->9->10,11->12->13,14,15]

Normal



Duration of each activity: [2,4,1,2,3,4,5,2,2,1,3,2,4,2,3]

1. Develop strategy for schedule compression by identifying knowledge area(s) with valid input, tools & techniques and outputs. [5]
2. Show new activity Timeline/Gantt chart after sequencing activities. [5]

3. Develop Critical path to estimate the duration using AoA. [3]
4. After reaching the completion of activity 7, it has been observed that it took 3 more units in duration, what will be the new duration of the project. [2]
5. Develop Phase Oriented WBS and WBS dictionary of the given scenario using Top-Down Approach. [5]
6. Choose at least 5 activities from the given case study or based on your assumption and define SIPOC for each. [5]

Note: Consider the actual remaining work and ideal remaining work for the problem.

Question. 02

[Marks: 5]

CLO: <2>; **Bloom Taxonomy Level:** <Understanding>

The Comsats University management implements the new version of Student Portal for the academic session of Spring 2024. During this session, management was feedbacked with several complaints by different users of the system. The feedback report is as follows.

Users	Complaint	# of complaints
Students	Login issues	20
Faculty	Slow response time	15
Finance/Exam	Generated reports are wrong	8
Management	Forget username/password	5
Students	Result is delayed	30
Students	404 page not found error	22
Faculty	Wrong credentials accepted	

You are required to identify the root causes using fish bone diagram.

Question. 03

[Marks: 10]

CLO: <3>; **Bloom Taxonomy Level:** <Creating>

1. Identify FS, FF, SS, SF among the following: [5]
 1. Baking the cake cannot be finished until the timer goes off.
 2. Complete the final FYP report till all the sections have been proofread.
 3. Do not prepare the sauce unless you start boiling the pasta.
 4. The emergency power supply won't turn off till the main power has been restored.
 5. Assemble the furniture to decorate the room.
2. Why discretionary dependencies are documented and further processed while they can be neglected? [2]
3. Explain each document's purpose in one line statement: [3]
 1. Project Charter
 2. Assumption log
 3. Change log
